ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	TERM 1 : AUTUMN	50 days?	Mon 03/10/05	Fri 09/12/05		
2	AUTUMN HOLIDAY	21 days?	Sat 10/12/05	Sun 08/01/06	1	
3	TERM 2 : SPRING	50 days?	Mon 09/01/06	Fri 17/03/06	2	
4	SPRING HOLIDAY	23 days?	Sat 18/03/06	Tue 18/04/06	3	
5	TERM 3 : SUMMER	48 days?	Wed 19/04/06	Fri 23/06/06	4	
6	Initial Research	13 days?	Mon 03/10/05	Wed 19/10/05		
7	**PROJECT PROPOSAL (MILESTONE)**	**0 days**	**Thu 20/10/05**	**Thu 20/10/05**	**6**	
8	**SERVER DEVELOPMENT (PHASE)**	**51 days?**	**Mon 24/10/05**	**Fri 30/12/05**		
9	Miscellaneous GUI Component Development (Including DEMO)	10 days?	Mon 24/10/05	Fri 04/11/05		
10	Implement Simple Version Of .NET Remoting (Client and Server)	5 days?	Mon 07/11/05	Fri 11/11/05	9	
11	Create MP3 Editor Control	5 days?	Mon 14/11/05	Fri 18/11/05	10	
12	Create Player Control	5 days?	Mon 28/11/05	Fri 02/12/05	26	
13	Create Media Library Database	3 days?	Thu 08/12/05	Sat 10/12/05	27	
14	Create Media Library Control	15 days?	Mon 12/12/05	Fri 30/12/05	13	
15	**CLIENT DEVELOPMENT PHASE**	**25 days?**	**Mon 02/01/06**	**Fri 03/02/06**		
16	Creation Of IP Address Browsing Code	5 days?	Mon 02/01/06	Fri 06/01/06	14	
17	Creation of Client GUI (Using some re-usable code from server development)	10 days?	Mon 09/01/06	Fri 20/01/06	16	
18	Create of Full Blown .NET Remoting Client Commands	10 days?	Mon 23/01/06	Fri 03/02/06	17	
19	**EXTRA's PHASE (MAY NOT GET TO DO THESE, TIME PERMITTING)**	**15 days?**	**Mon 06/02/06**	**Fri 24/02/06**		
20	CD Rip To WAV	5 days?	Mon 06/02/06	Fri 10/02/06		
21	Direct X Recording WAV (Through Sound Card)	5 days?	Mon 13/02/06	Fri 17/02/06	20	
22	WAV to MP3	5 days?	Mon 20/02/06	Fri 24/02/06	21	
23	**TESTING PHASE**	**16 days?**	**Mon 06/03/06**	**Fri 24/03/06**		
24	Creation Of Test Specification	5 days?	Mon 06/03/06	Fri 10/03/06	30	
25	Function Point Testing	**8 days?**	**Thu 16/03/06**	**Fri 24/03/06**	**31**	
26	Creation Of Interim Report	5 days?	Mon 21/11/05	Fri 25/11/05	11	
27	**INTERIM REPORT (MILESTONE)**	0 days	Thu 08/12/05	Thu 08/12/05	29	
28	Supervisor Approval Period (1 WEEK)	5 days?	Mon 28/11/05	Fri 02/12/05	26	
29	Review and Incorporate Supervisor Comments	3 days?	Mon 05/12/05	Wed 07/12/05	28	
30	Creation Of Draft Report	5 days?	Mon 27/02/06	Fri 03/03/06		
31	**DRAFT REPORT (MILESTONE)**	**0 days**	**Thu 16/03/06**	**Thu 16/03/06**	**33**	
32	Supervisor Approval Period (1 WEEK)	5 days?	Mon 06/03/06	Fri 10/03/06	30	
33	Review and Incorporate Supervisor Comments	3 days?	Mon 13/03/06	Wed 15/03/06	32	
34	Creation Of Final Report	10 days?	Mon 27/03/06	Fri 07/04/06	25	
35	**FINAL REPORT (MILESTONE)**	**0 days**	**Thu 27/04/06**	**Thu 27/04/06**	**37**	
36	Supervisor Approval Period (1 WEEK)	5 days?	Mon 10/04/06	Fri 14/04/06	34	
37	Review and Incorporate Supervisor Comments	3 days?	Mon 17/04/06	Wed 19/04/06	36	
38	Prepare Presentation / Ensure System Function Ponits Are Working at UNI	5 days	Thu 20/04/06	Wed 26/04/06	37	
39	**PROJECT PRESENTATION (MILESTONE)**	10 days?	Mon 01/05/06	Fri 12/05/06	38	
40	**MEET SUPERVISOR (Recurring Meeting Once Per Week)**	**192 days**	**Mon 03/10/05**	**Mon 26/06/06**		

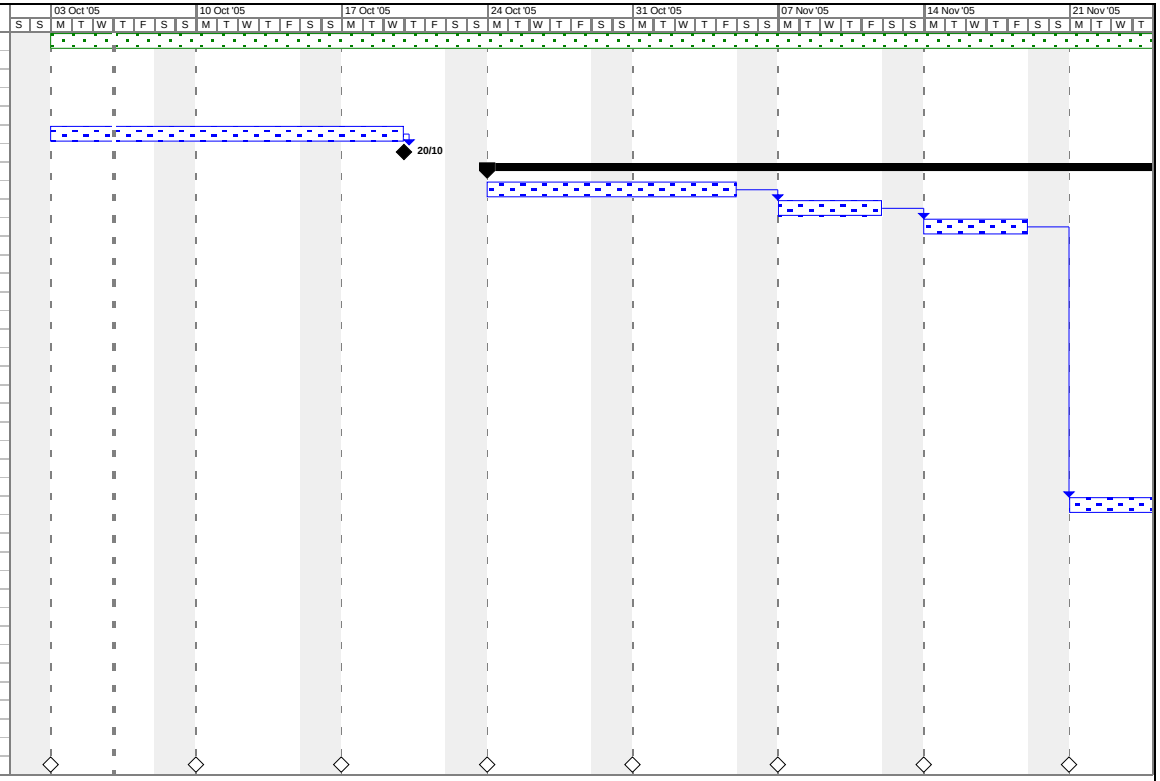

Project: sb54_ProjectGannt_v1
Date: Thu 06/10/05

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

ID	Task Name	Duration
1	TERM 1 : AUTUMN	50 days?
2	AUTUMN HOLIDAY	21 days?
3	TERM 2 : SPRING	50 days?
4	SPRING HOLIDAY	23 days?
5	TERM 3 : SUMMER	48 days?
6	Initial Research	13 days?
7	**PROJECT PROPOSAL (MILESTONE)**	**0 days**
8	**SERVER DEVELOPMENT (PHASE)**	**51 days?**
9	Miscellaneous GUI Component Development (Including DEMO)	10 days?
10	Implement Simple Version Of .NET Remoting (Client and Server)	5 days?
11	Create MP3 Editor Control	5 days?
12	Create Player Control	5 days?
13	Create Media Library Database	3 days?
14	Create Media Library Control	15 days?
15	**CLIENT DEVELOPMENT PHASE**	**25 days?**
16	Creation Of IP Address Browsing Code	5 days?
17	Creation of Client GUI (Using some re-usable code from server development)	10 days?
18	Create of Full Blown .NET Remoting Client Commands	10 days?
19	**EXTRA's PHASE (MAY NOT GET TO DO THESE, TIME PERMITTING)**	**15 days?**
20	CD Rip To WAV	5 days?
21	Direct X Recording WAV (Through Sound Card)	5 days?
22	WAV to MP3	5 days?
23	**TESTING PHASE**	**16 days?**
24	Creation Of Test Specification	5 days?
25	Function Point Testing	**8 days?**
26	Creation Of Interim Report	5 days?
27	**INTERIM REPORT (MILESTONE)**	0 days
28	Supervisor Approval Period (1 WEEK)	5 days?
29	Review and Incorporate Supervisor Comments	3 days?
30	Creation Of Draft Report	5 days?
31	**DRAFT REPORT (MILESTONE)**	**0 days**
32	Supervisor Approval Period (1 WEEK)	5 days?
33	Review and Incorporate Supervisor Comments	3 days?
34	Creation Of Final Report	10 days?
35	**FINAL REPORT (MILESTONE)**	**0 days**
36	Supervisor Approval Period (1 WEEK)	5 days?
37	Review and Incorporate Supervisor Comments	3 days?
38	Prepare Presentation / Ensure System Function Ponits Are Working at UNI	5 days
39	**PROJECT PRESENTATION (MILESTONE)**	10 days?
40	**MEET SUPERVISOR (Recurring Meeting Once Per Week)**	**192 days**

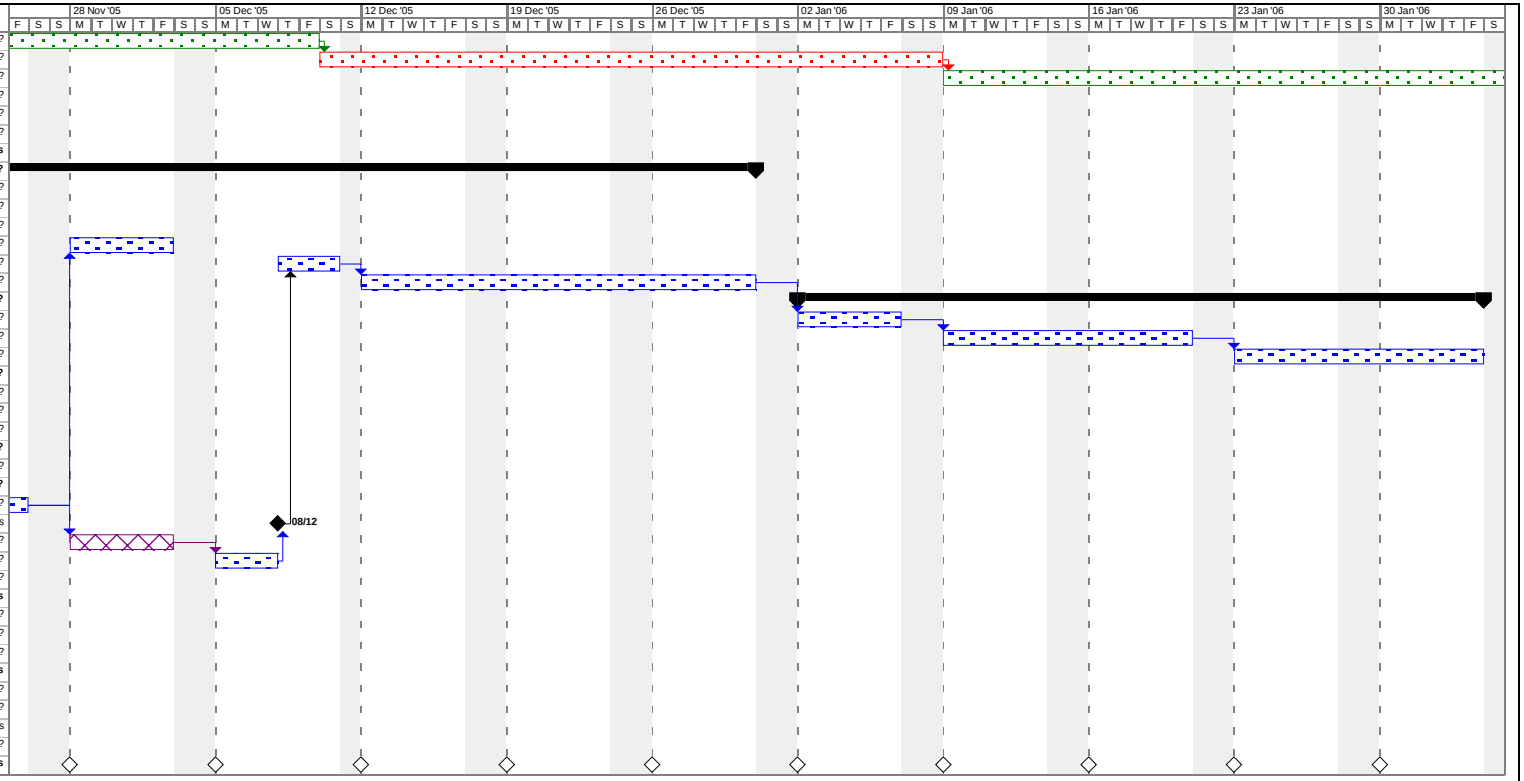

Project: sb54_ProjectGannt_v1
Date: Thu 06/10/05

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

ID	Task Name	Duration
1	TERM 1 : AUTUMN	50 days?
2	AUTUMN HOLIDAY	21 days?
3	TERM 2 : SPRING	50 days?
4	SPRING HOLIDAY	23 days?
5	TERM 3 : SUMMER	48 days?
6	Initial Research	13 days?
7	**PROJECT PROPOSAL (MILESTONE)**	**0 days**
8	**SERVER DEVELOPMENT (PHASE)**	**51 days?**
9	Miscellaneous GUI Component Development (Including DEMO)	10 days?
10	Implement Simple Version Of .NET Remoting (Client and Server)	5 days?
11	Create MP3 Editor Control	5 days?
12	Create Player Control	5 days?
13	Create Media Library Database	3 days?
14	Create Media Library Control	15 days?
15	**CLIENT DEVELOPMENT PHASE**	**25 days?**
16	Creation Of IP Address Browsing Code	5 days?
17	Creation of Client GUI (Using some re-usable code from server development)	10 days?
18	Create of Full Blown .NET Remoting Client Commands	10 days?
19	**EXTRA's PHASE (MAY NOT GET TO DO THESE, TIME PERMITTING)**	**15 days?**
20	CD Rip To WAV	5 days?
21	Direct X Recording WAV (Through Sound Card)	5 days?
22	WAV to MP3	5 days?
23	**TESTING PHASE**	**16 days?**
24	Creation Of Test Specification	5 days?
25	Function Point Testing	**8 days?**
26	Creation Of Interim Report	5 days?
27	**INTERIM REPORT (MILESTONE)**	0 days
28	Supervisor Approval Period (1 WEEK)	5 days?
29	Review and Incorporate Supervisor Comments	3 days?
30	Creation Of Draft Report	5 days?
31	**DRAFT REPORT (MILESTONE)**	**0 days**
32	Supervisor Approval Period (1 WEEK)	5 days?
33	Review and Incorporate Supervisor Comments	3 days?
34	Creation Of Final Report	10 days?
35	**FINAL REPORT (MILESTONE)**	**0 days**
36	Supervisor Approval Period (1 WEEK)	5 days?
37	Review and Incorporate Supervisor Comments	3 days?
38	Prepare Presentation / Ensure System Function Ponits Are Working at UNI	5 days
39	**PROJECT PRESENTATION (MILESTONE)**	10 days?
40	**MEET SUPERVISOR (Recurring Meeting Once Per Week)**	**192 days**

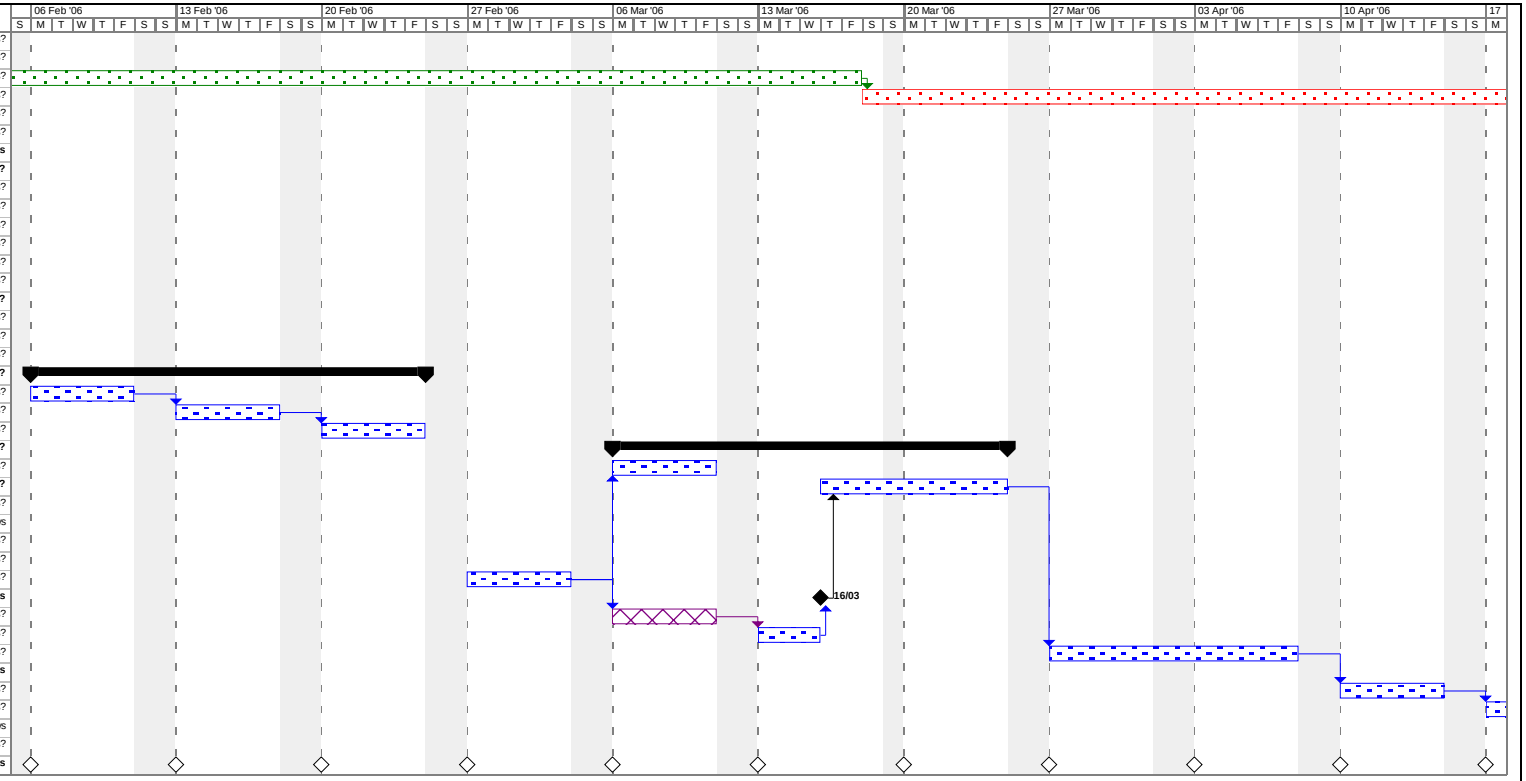

Project: sb54_ProjectGannt_v1
Date: Thu 06/10/05

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

ID	Task Name	Duration
1	TERM 1 : AUTUMN	50 days?
2	AUTUMN HOLIDAY	21 days?
3	TERM 2 : SPRING	50 days?
4	SPRING HOLIDAY	23 days?
5	TERM 3 : SUMMER	48 days?
6	Initial Research	13 days?
7	**PROJECT PROPOSAL (MILESTONE)**	**0 days**
8	**SERVER DEVELOPMENT (PHASE)**	**51 days?**
9	Miscellaneous GUI Component Development (Including DEMO)	10 days?
10	Implement Simple Version Of .NET Remoting (Client and Server)	5 days?
11	Create MP3 Editor Control	5 days?
12	Create Player Control	5 days?
13	Create Media Library Database	3 days?
14	Create Media Library Control	15 days?
15	**CLIENT DEVELOPMENT PHASE**	**25 days?**
16	Creation Of IP Address Browsing Code	5 days?
17	Creation of Client GUI (Using some re-usable code from server development)	10 days?
18	Create of Full Blown .NET Remoting Client Commands	10 days?
19	**EXTRA's PHASE (MAY NOT GET TO DO THESE, TIME PERMITTING)**	**15 days?**
20	CD Rip To WAV	5 days?
21	Direct X Recording WAV (Through Sound Card)	5 days?
22	WAV to MP3	5 days?
23	**TESTING PHASE**	**16 days?**
24	Creation Of Test Specification	5 days?
25	Function Point Testing	**8 days?**
26	Creation Of Interim Report	5 days?
27	**INTERIM REPORT (MILESTONE)**	0 days
28	Supervisor Approval Period (1 WEEK)	5 days?
29	Review and Incorporate Supervisor Comments	3 days?
30	Creation Of Draft Report	5 days?
31	**DRAFT REPORT (MILESTONE)**	**0 days**
32	Supervisor Approval Period (1 WEEK)	5 days?
33	Review and Incorporate Supervisor Comments	3 days?
34	Creation Of Final Report	10 days?
35	**FINAL REPORT (MILESTONE)**	**0 days**
36	Supervisor Approval Period (1 WEEK)	5 days?
37	Review and Incorporate Supervisor Comments	3 days?
38	Prepare Presentation / Ensure System Function Ponits Are Working at UNI	5 days
39	**PROJECT PRESENTATION (MILESTONE)**	10 days?
40	**MEET SUPERVISOR (Recurring Meeting Once Per Week)**	**192 days**

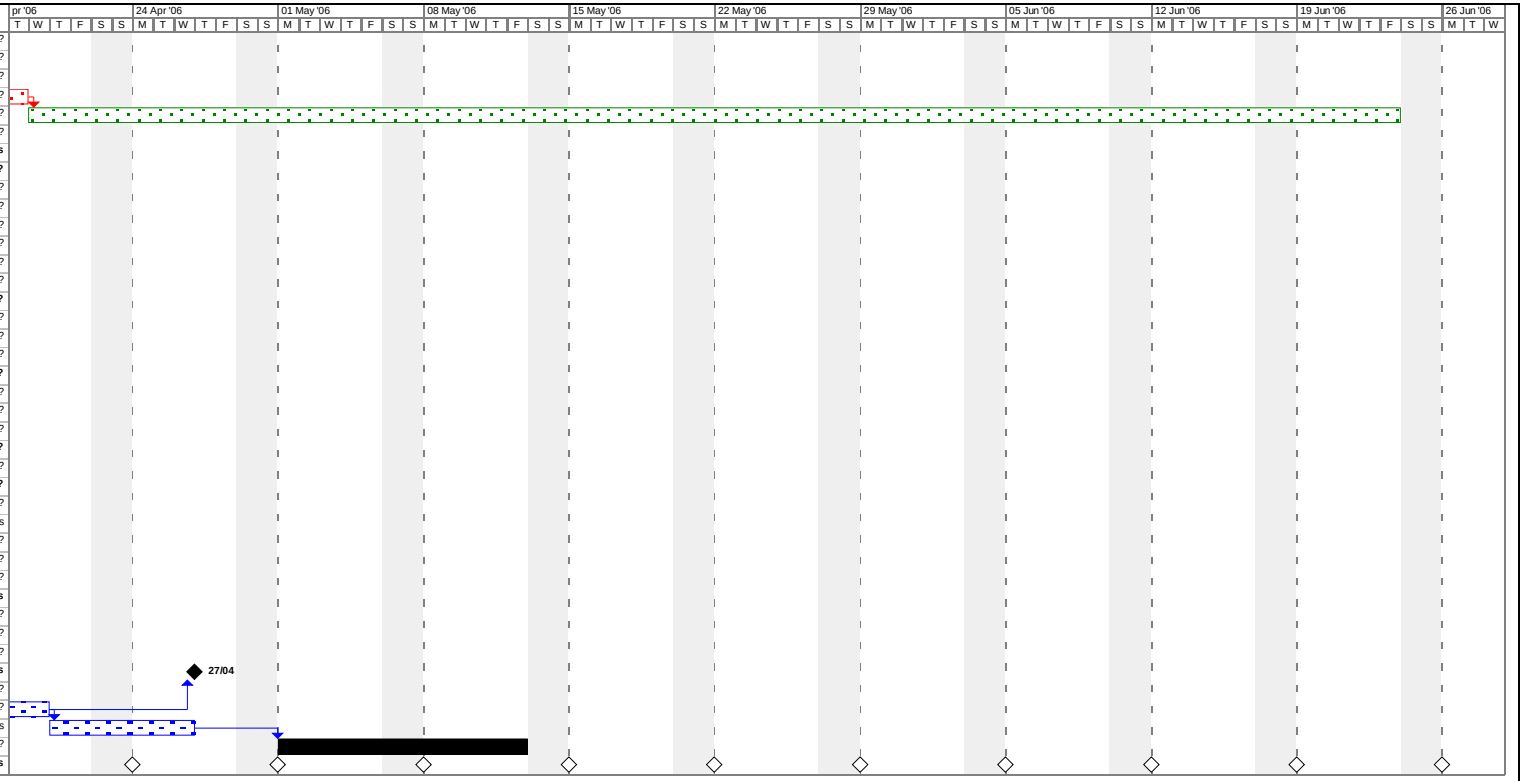

Project: sb54_ProjectGannt_v1
Date: Thu 06/10/05

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
